

Our Future Water Supply

The Willamette Water Supply System Commission (WWSS Commission) is an Oregon intergovernmental entity formed by Tualatin Valley Water District (TVWD), the City of Hillsboro, and the City of Beaverton. The WWSS Commission was formed to build the Willamette Water Supply System (WWSS) in response to planned growth in their service areas. TVWD has been designated the Managing Agency for the WWSS Commission, and TVWD operates the Willamette Water Supply Program (WWSP) to plan, design, and construct the WWSS. The WWSS will provide an additional resilient water supply for Washington County. When complete, the WWSS will be one of Oregon's most seismically-resilient water systems—built to better withstand natural disasters, protect public health, and speed regional economic recovery through restoring critical services more quickly. The new system will be completed by 2026.


Willamette Water Supply

Our Reliable Water

Monthly Progress Report

Month End April 2020

Raw Water Facilities Phase 1 Construction

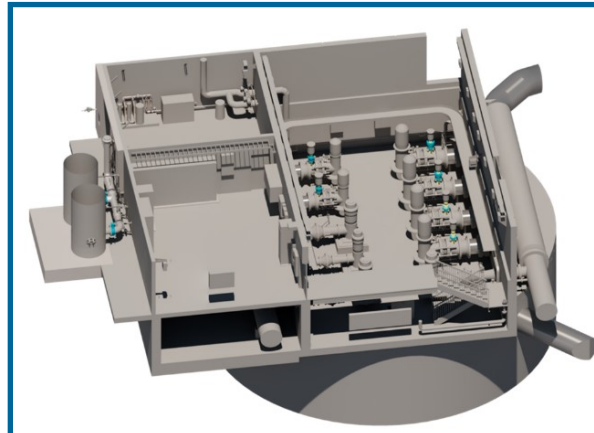

Raw Water Pump Station and Caisson

The Willamette Water Supply System (WWSS) Raw Water Facilities (RWF_1.0) project will modify the existing raw water pump station and intake

infrastructure at the Willamette River Water Treatment Plant (WRWTP) in Wilsonville. Over the last several months, the RWF Construction Manager/General Contractor (CM/GC), Kiewit Infrastructure West Co., has been developing a guaranteed maximum price (GMP) for the first of two phases of construction. Phase 1 consists of modifying the existing intake and pump station, installing seismic mitigation measures, adding pumping capacity, adding electrical improvements, and constructing a large-diameter raw water pipeline. Construction of Phase 1 is anticipated to begin June 2020 and continue to February 2022.

Safety On-site, Safety at Home

Every day, Willamette Water Supply Program (WWSP) staff, contractors, and leaders make decisions to support keeping people safe. The WWSP Health & Safety Team and contractors have implemented practices that will help keep contractors and staff safe while continuing construction of the WWSS as the COVID-19 outbreak evolves.

The team continues to operate and construct under the State of Oregon's "Stay Home, Save Lives" mandates. Our practices will be modified as this crisis evolves.

The team will continue to develop, share, and require mitigating actions to protect WWSP staff and contractors while continuing essential construction of the WWSS to achieve completion in 2026.

WWSS Response to COVID-19

The WWSP team has responded to the COVID-19 outbreak in the following ways:

- Developed a COVID-19 plan that recognizes potential business disruptions and health and safety impacts on WWSP construction crews.
- Organized weekly information and outreach training (remotely or social distancing) as information became available from the World Health Organization and Centers for Disease Control.
- Updated guidelines and staff training, and supported contractors to expand safe work practices for everyday tasks.
- Tracked best management practices and implemented actions that advance the WWSP COVID-19 mitigation strategy.

Procurement & Business Opportunities

The WWSP staff are preparing for several upcoming professional services and construction contractor procurements. Listed below are active procurements and upcoming events and procurements. Procurement opportunities are also published at <http://www.ourreliablewater.org/business-opportunities>.

Active Procurements


- None at this time

Upcoming Procurements

- Tualatin-Sherwood Area Pipeline (PLM_4.1)
Construction Invitation to Bid (ITB) by Washington County (Quarter 4, 2020)

Schedule Summary


WWSP design and planning began in 2013; the Willamette Water Supply System is expected to be in service by July 2026. Below are the major milestones and activities forecasted from 2020 to 2023*. The WWSP team is committed to on-time delivery. See page 4 for descriptions of the projects referenced below.

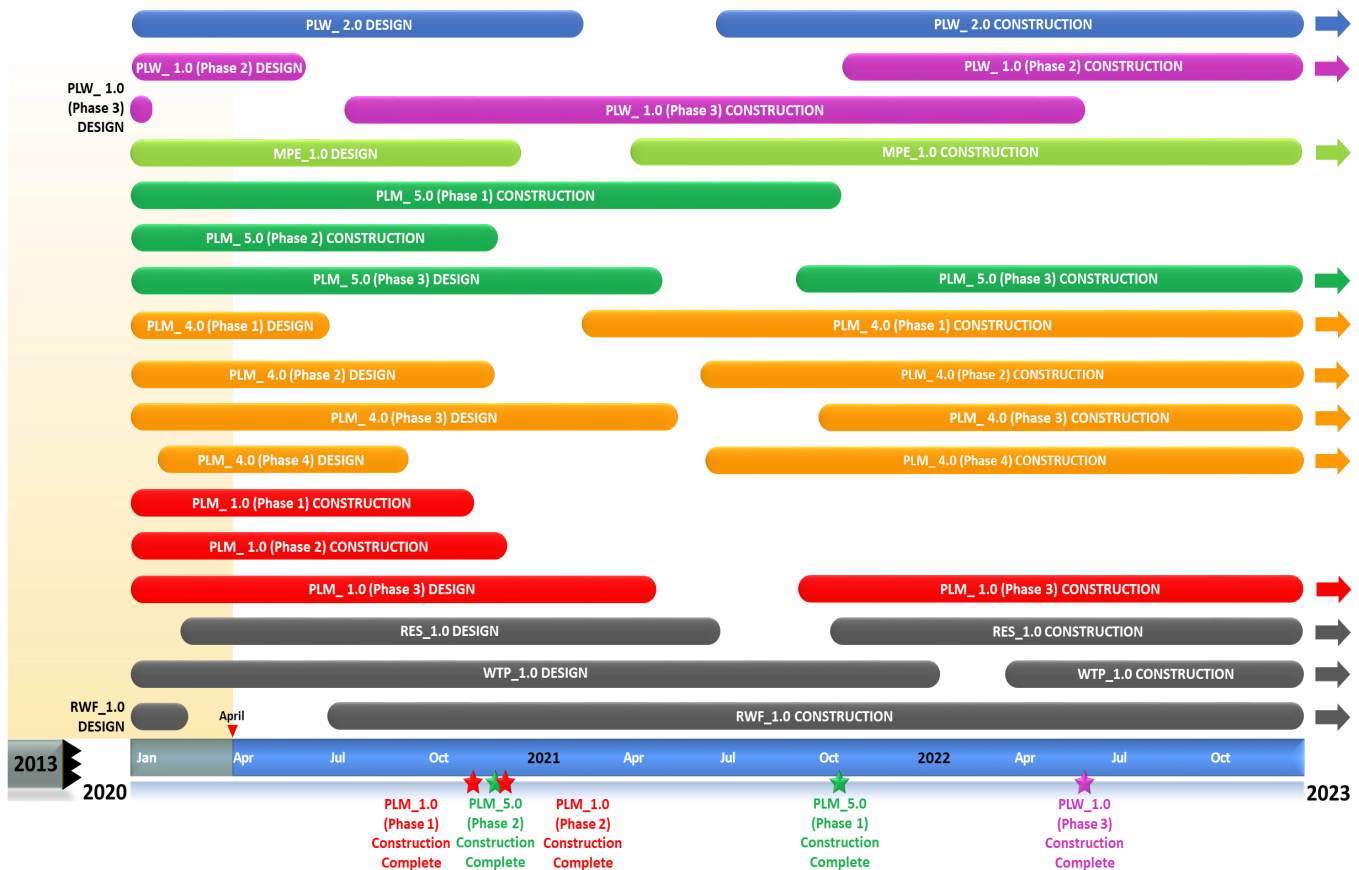

*The actual order and duration of projects continues to be refined and is subject to change.

Forecast Cost Summary

The graph below illustrates the projected WWSP cash flow by fiscal year (FY July 1 to June 30)*. The cumulative cash flow establishes the budgeted \$1.3 billion, which accounts for actual and current projected costs, including projected escalation in the cost of labor, materials, and equipment required to build WWSP projects.

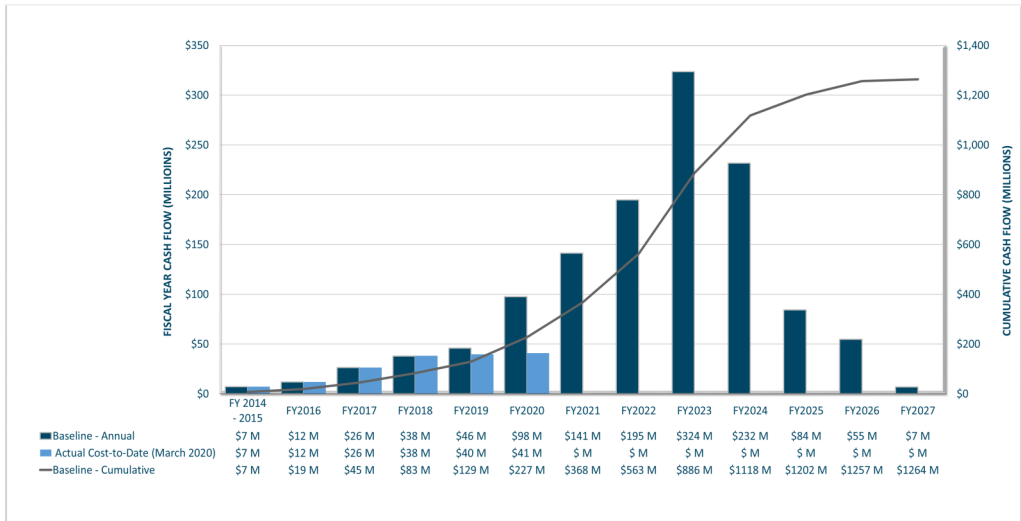


Costs to date for FY 2020 are \$41 million. Cumulative costs are projected to be \$227 million through the end of FY 2020.


**Data continues to be refined and is subject to change.*

Cumulative Cost Summary

WWSP cumulative costs are tracked and updated monthly. The chart below summarizes the distribution of cumulative costs through March 2020.

Cumulative Water Supply Program costs to date are approximately \$164 million, with the majority spent on planning, engineering, construction, and real estate activities.

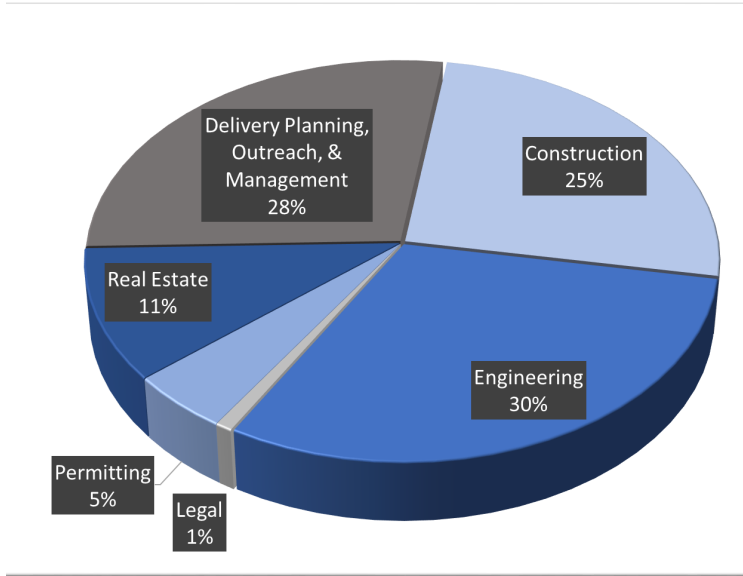

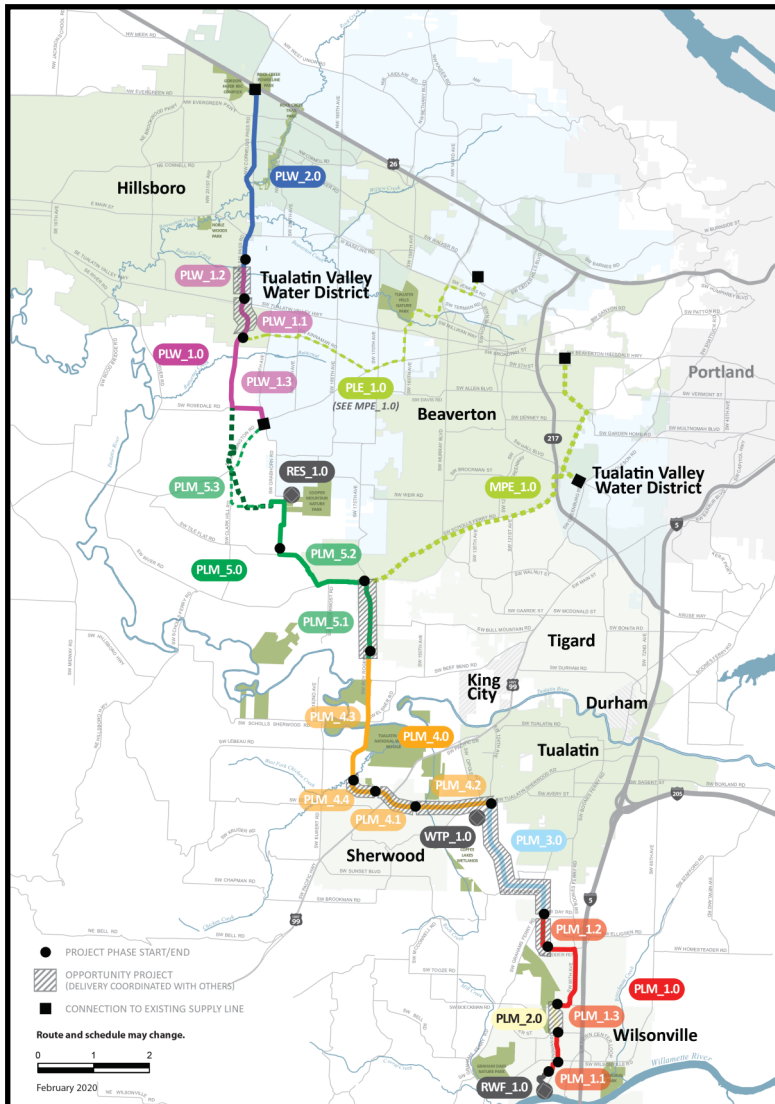

- WTP_1.0 Willamette Water Supply System Water Treatment Plant (Water Treatment Plant (WTP))**
Description: 60-million gallon per day water treatment plant (WTP_1.0), including a finished water pump station (FPS_1.0) and a control system (DCS_1.0) located near Sherwood.
Status: Design Phase (WTP/FPS Construction Start: 03/2022) Design Phase (DCS Construction Start: 03/2022)
- FPS_1.0**
- DCS_1.0**
- RWF_1.0 Raw Water Facilities Expansion (Raw Water Facilities (RWF) Expansion)**
Description: Expansion of the existing raw water pump station and intake at the Willamette River WTP (WRWTP) in Wilsonville to 60 million gallons per day of initial capacity for the Willamette Water Supply System.
Status: Design Phase (Construction Start: 06/2020)

The mid-Willamette River at Wilsonville is the supply source for the WWSS. The system consists of modifying the existing river intake and expanding pumping capacity, building more than 30 miles of drinking water pipeline, reservoir storage facilities on Cooper Mountain, and a new WTP in Sherwood.

For more information about the WWSP, visit www.ourreliablewater.org or call 503.941.4570.

PLW_2.0 Cornelius Pass Pipeline Project (Frances Road to Highway 26)
Description: 3.3-mile water pipeline along Cornelius Pass Rd. from Frances St. to Hwy 26; connects to existing supply lines for City of Hillsboro and TVWD.
Status: Design Phase (Construction Start: 06/2021)

PLW_1.0 South Hillsboro Area Pipeline Project (Farmington Road to Frances Street)
Description: 3.9-mile water pipeline from SW Farmington Rd. at SW 209th Ave. to Cornelius Pass Rd. at Frances St.
Status: Construction Phase (Phase 1: Complete; Phase 2 Start: 11/2021; Phase 3 Start: 07/2020)

MPE_1.0 Metzger Pipeline East Project (Roy Rogers Road to Beaverton Hillsdale Hwy)
Description: 7.3-mile water pipeline to be built in lieu of PLE_1.0 along SW Scholls Ferry Rd. between SW Roy Rogers Rd. and Allen Blvd.; connects to Metzger service area at SW Oleson Rd. and TVWD's system.
Status: Design Phase (Construction Start: 05/2021)

RES_1.0 South Beaverton Area Water Storage Tanks (Storage Tanks)
Description: Two 15-million gallon storage tanks located on Cooper Mountain.
Status: Design Phase (Construction Start: 09/2021)

PLM_5.0 Scholls Area Pipeline Project (North of Beef Bend Road to Farmington Road)
Description: 7.2-mile water pipeline from SW Roy Rogers Rd. 0.5-mile north of SW Beef Bend Rd. to SW Farmington Rd. at SW 209th Ave.
Status: Construction Phase (Phase 1 Complete: 10/2021; Phase 2 Complete: 11/2020; Phase 3 Start: 09/2021)

PLM_4.0 Tualatin-Sherwood Area Pipeline Project (SW 124th Avenue to north of Beef Bend Road)
Description: 5.3-mile water pipeline from 124th Ave. at SW Tualatin Sherwood Rd. along SW Roy Rogers Rd. to 0.5 miles north of SW Beef Bend Rd.
Status: Design Phase (Phase 1 Construction Start: 02/2021; Phase 2 Start: 06/2021; Phase 3 Start: 9/2021; Phase 4 Start: 6/2021)

PLM_3.0 124th Avenue Partnership Project (SW 124th Avenue Extension)
Description: 2.7-mile water pipeline from Grahams Ferry Rd. at Day Rd. to 124th Ave. at SW Tualatin Sherwood Rd.
Status: Complete

PLM_2.0 Kinsman Road Partnership Project (Kinsman Road Extension)
Description: 0.5-mile water pipeline along Kinsman Rd. between Barber St. and Boeckman Rd.
Status: Complete

PLM_1.0 Wilsonville Area Pipeline Project (WRWTP to Day Road)
Description: 3.3-mile water pipeline from WRWTP to the intersection of SW Garden Acres Rd. at Day Rd.
Status: Construction Phase (Phase 1 Complete: 10/2020; Phase 2 Complete: 11/2020; Phase 3 Start: 9/2021)
